
ACPS Capital Improvement Program (CIP) Quarterly Project Status Report FY 2019 Quarter 1 (July – September)

December 2018 School Board Meeting



Every Student Succeeds

ACPS 2020 Strategic Plan Goals

- Goal 1 Academic Excellence and Educational Equity: Every student will be academically successful and prepared for life, work, and college.
- **Goal 2 Family and Community Engagement:** ACPS will partner with families and the community in the education of Alexandria's youth.
- **Goal 3 An Exemplary Staff:** ACPS will recruit, develop, support, and retain a staff that meets the needs of every student.
- Goal 4 <u>Facilities and the Learning</u> <u>Environment:</u> ACPS will provide optimal and equitable learning environments.
- **Goal 5 Health and Wellness:** ACPS will promote efforts to enable students to be healthy and ready to learn.
- **Goal 6 <u>Effective and Efficient Operations:</u>** ACPS will be efficient, effective, and transparent in its business operations.






Q1 Quarterly Report Financial Summary

TOTAL Q1 FY 2019 EXPENDITURES/COMMITMENTS \$58,294,508


The top five CIP Expenditures and Commitments during Q1 FY 2019:

26% 58% - Paid Invoices - Outstanding Invoices - Open Purchase Orders

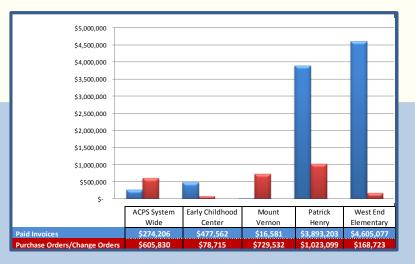

3

The total approximate CIP Budget Balance to Year End = \$45,856,891

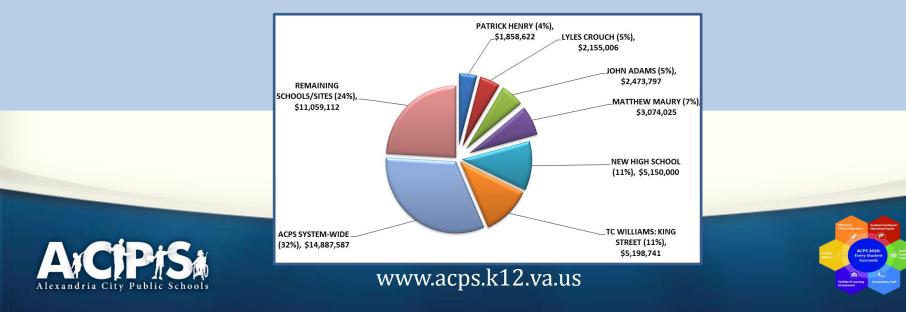

Ferdinand T. Day School

Progress through Q1:


Construction:

- **Reached** substantial ٠ completion
- Conducted ribbon cutting ٠ ceremony

Anticipated Progress through Q2:

- Continue work on building commissioning
- Continue work on punch list ٠ and close-out





Patrick Henry PK-8 School

Progress through Q1:

Construction:

- Construction continued on building
- Completed FF&E
 procurement

Anticipated Progress through Q2:

- Community meeting
- Verify and update logistics move-in plan









Retrofitting for Co-Location Pre K Center

Progress through Q1:

• Project reached substantial completion for use at the start of the school year.

Anticipated Progress through Q2:

• Planning for phase II



New Administrative areas to support both Pre-K and K through 5





www.acps.k12.va.us



Renovated Pre-K Classroom with new restrooms



New cubbies and storage space off of corridor



New Teachers Lounge

Mount Vernon Playground

Progress through Q1:


• Continued construction in anticipation of project completion in December.

Anticipated Progress through Q2:

 Continue construction administration on project and provide bi-weekly updates to school









https://www.acps.k12.va.us/Page/2162: Faculty and PTA Presentation - March 2018 (PDF)





Francis Hammond Kitchen Cafeteria Renovation

Progress through Q1:

 Project reached substantial completion in order to be used at start of school year

Anticipated Progress through Q2:

 Continue punch list and on cafeteria and provide additional work to upgrade kitchen.





GW Kitchen Cafeteria Renovation

Progress through Q1:


- Contract for art work and furniture was finalized
- Construction continued on the kitchen and cafeteria


Anticipated Progress through Q2:

Substantial Completion and full use of the space







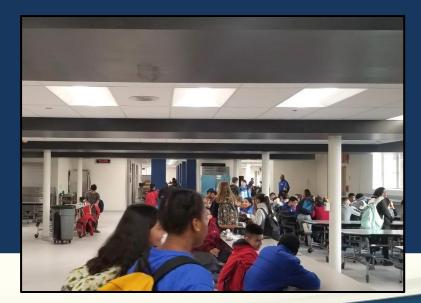





T.C. Williams Stadium Design





Progress through Q1:

Modernize the Stadium:

• DSUP was approved in order to move forward with completing construction documents and applying for a building permit.

Anticipated Progress through Q2:

• Continued community engagement and review of the design in preparation for school board update and permitting.







Questions?

Elijah Gross Director of Planning, Design and Construction <u>elijah.gross@acps.k12.va.us</u> 703-619-8294, ext.1258



Superintendent Dr. Gregory C. Hutchings, Jr. **School Board** Ramee A. Gentry, *Chair* Cindy Anderson, *Vice Chair* Ronnie Campbell William E. Campbell Hal E. Cardwell Karen A. Graf Christopher J. Lewis Margaret Lorber Veronica Nolan

11
