

Department of Facilities and Operations

Summer Projects Update

School Board Meeting
September 17, 2020



EQUITY FOR ALL 2025

Essential Questions

1) What projects were initiated and/or completed?

2) What projects are ongoing?

3) What are next steps?

Douglas MacArthur

DM at Taney Ave

- Interior Renovation reached substantial completion
 - Auditorium renovated to a gymnasium
 - HVAC repaired
 - Complete re-painting of building
- Exterior Renovation nearing completion
 - New parking lot and loop installed
 - Sidewalk and entrances upgraded
- Relocation
 - All items needed for DM moved from old building

New DM

- Design Development Phase Finalized and Approved for Hearing
- Engagement Continued: 2 Advisory Group Meetings, 1 Community Feedback Event, 1 Community Meeting, 1 School Team Meeting
- Value Management Activities and Cost Estimating
- Net-Zero Energy Ready Charrettes



Next Steps (Fall 2020)

Douglas MacArthur at Taney Ave

- Final building details and cleaning: minor roof repair, kitchen equipment setup, phone line and fire alarm connection approval

New Douglas MacArthur

- Demolition and abatement package being prepared for old building
- Interior furniture and finishes finalized
- Playground equipment selection

Building Systems Projects

Francis Hammond

Roof Replacement: D-
Wing, Music Wing

Status: Planning/Design
completed over the
summer. Construction
beginning mid-
September

HVAC: Replacement of
AHUs & pumps

Status: Design initiated
and is ongoing

George Washington

Roof Replacement: B
and C-Wings

Status: Design
completed.
Construction to
commence in next two
weeks

HVAC: A-Wing Design
Status: Design initiated;
completed by October.
Repairs anticipated to
start November

John Adams

Roof Replacement:
Phase I -
Kitchen/Cafeteria, ECC

Status: Construction
substantially complete.
Phase II has
commenced and
anticipated to be
completed by
December

Matthew Maury

Roof Replacement:
North Classrooms,
Kitchen

Status: ITB initiated and
completed; awaiting
award

HVAC Replacement:
New RTUs

Status:
Construction
commenced. Materials
have arrived;
anticipated completion
by October

Mount Vernon

HVAC: Cooling Tower &
pumps replacement

Status: Design
completed. Submitting
for permit;
construction to
commence Winter
2020

William Ramsay

Roof Replacement: East
Classrooms,
Auditorium


Status: Phase I Roof
substantially complete;
anticipate completion
Sept. Phase II to be
complete by December

HVAC: new RTUs

Status: Design
completed. Materials
arriving in coming
weeks; anticipated
completion by early
October

Flooring Projects


**Cora Kelly- 1st Floor
Hallway Before and
After**

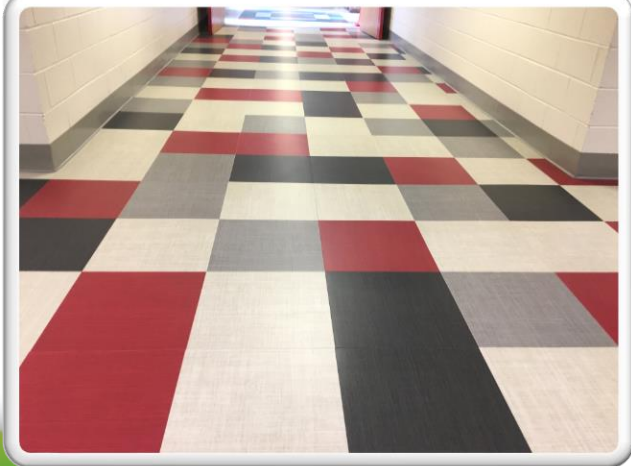

**Lyles Crouch- Classroom
Before and After**



**William Ramsay- Auditorium
Before and After**

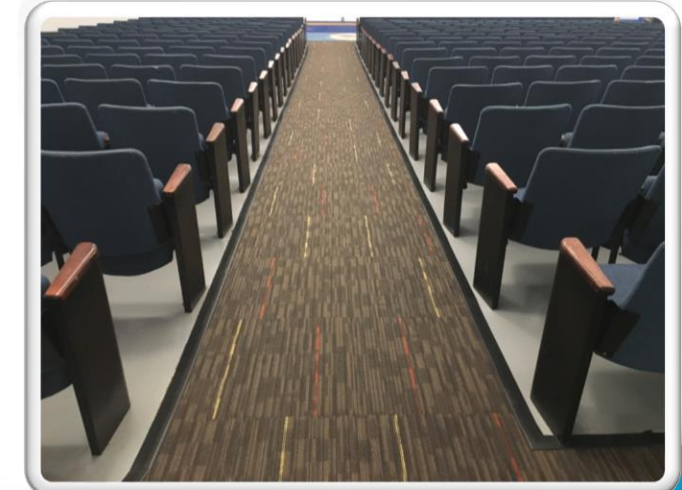

Notable Projects



**TC Williams Stadium
Renovation**

**(Phase I: Fall; Phase II: Spring
Completion)**



**Kitchen and Servery
Upgrades**

**(Cora Kelly and John Adams
close-out)**



FTD Elevated Gym

(March Completion)

Next Steps (Fall 2020)

Summer Projects:

- Close-out 48 Summer Projects

Building Systems:

- Combine phasing to advance roof projects completion
- Advance HVAC phases to prepare buildings for return

Flooring:

- Continue asbestos remediation at certain sites
- Implement additional flooring replacement projects to take advantage of reduced contractor costs

Building Envelope:

- Implement window replacement, waterproofing projects

Summer Cleaning

Summer was the “deep cleaning” period



- All schools had deep cleaning occur
- Some sections are still in the process of being deep cleaned due to awaiting completion of construction activities

Deep cleaning is extensive and an orchestrated sequence of events



- Routine cleaning** - cleaning of classrooms and common spaces, trash removal, dusting, sweeping, moping, vacuuming and cleaning and periodic disinfecting of hard surfaces such as desks, tables, and frequently-touched points
- “New” Enhanced cleaning** - routine cleaning plus increased bathroom cleaning and disinfecting throughout the day
- Deep cleaning** - enhanced cleaning plus walls, lamps, hard and soft surfaces, wiping down of electronics, shampooing carpet, stripping and waxing floors.

Questions?

Dr. Alicia Hart, Acting Executive Director of Facilities and Operations

alicia.hart@acps.k12.va.us

Erika Gulick, Director of Capital Programs, Planning and Design

erika.gulick@acps.k12.va.us

John Finnigan, Acting Director of Educational Facilities

john.finnigan@acps.k12.va.us

Anita Cordova, Director of Maintenance and Custodial Services

anita.cordova@acps.k12.va.us

Superintendent

Dr. Gregory C. Hutchings,
Jr.

School Board

Cindy Anderson, *Chair*
Veronica Nolan, *Vice Chair*

Meagan L. Alderton

Ramee A. Gentry

Jacinta Greene

Margaret Lorber

Michelle Rief
